

11 EXAMPLE WAY, SCOTLAND, ML2 2IT

4 Bed Detached

Example Homes

Mr and Mrs Example

Chartered Building Surveyor Best Snag Scotland 14 Jun 2023

Project Details

Mr and Mrs Example Name: 11 Example Way, Scotland, ML2 2IT Client Name:

Summary: 4 Bed Detached Client Telephone: 07722113344

example@gmail.com Reference: **Example Homes** Client Email:

Weather - Generally dry and overcast with intermittent light rain. Description: Auditor Company: Best Snag Scotland

Status: New (20 May 2023) Auditor Name: Chartered Building Surveyor

Total Issues: 147

Filters Applied:

Issues: 1 to 146



Location: Hall

Description: Front door - hinge cover caps missing



Location: Hall

Description: Front door frame - protection not removed behind hinges





Location: Hall

Description: Front door - poor decorative finish to low level



Location: Hall

Description: Front door - left hand side glazing bead- poor decorative finish to head



Location: Hall

Description: Front door spyhole - glass scratched, evident when looking through.



Location: Hall

Description: Door - not sitting flush in head of frame.

Adjustment required



Location: Hall

Description: Front door threshold - chipped





Location: Hall

Description: Front door handle - paint overspilled



Location: Hall

Description: Waste water stack - access hatch missing . Required for maintenance.




Location: Hall

Description: Front door - reveal to head of door - not level



Location: Hall

Description: Ceiling - adjacent stair opening - plasterboard joints evident.

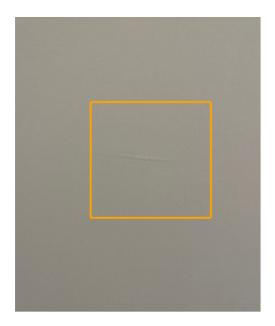

Location: Hall

Description: Wall - backing onto garage, approx 0.5m from front elevation - poor decorative finish



Location: Hall

Description: Kitchen door frame - left hand side, not caulked

Wall - left hand side of kitchen door frame - poor decorative finish





Location: Hall


Description: Walls - right hand side of kitchen door frame, low level - poor decorative finish



Location: Hall

Description: Wall - around light switch - poor decorative finish









Location: General

Description: General - radiators not level - review all and make good

- hall - utility

- en-suite

- bed 3



Location: Hall

Description: Wall - left hand side of newel post - poor decorative finish



Location: Hall


Description: Wall - below door bell chime- poor decorative finish






Location: Hall

Wall - right hand side of staircase - plasterboard joints and poor taping evident in 2no. Locations. Description:

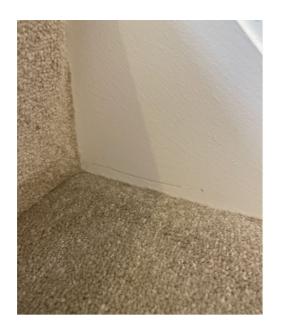







Location: Hall

Description: Both stair stringers - scored and chipped in a number of locations.

Review and make good decorative finish.



Location: Hall

Description: Stairs - movement underfoot when transversing stair and loud creaking noise evident.



Location: Hall 1st Floor

Description: Wall - above stair opening - plasterboard joint evident





Location: Hall 1st Floor

Description: Loft hatch - clean required



Location: Hall 1st Floor

Description: Ceiling - in front of bathroom door - plasterboard joint and exposed tape evident.



Location: Hall 1st Floor

Description: Window - glass outer pane - scratched as annotated





Location: Hall 1st Floor

Description: Window - external pvc frame - dirty and scratched in areas.

Clean and thereafter make good any damage.













Location: General

General - pvc window cills - tape not fully removed, dirty and numerous areas scratched. Description:

Clean and thereafter make good any damage.



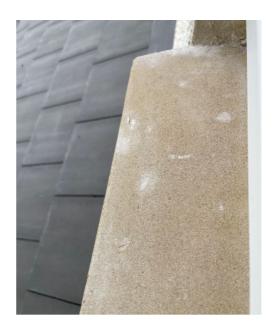

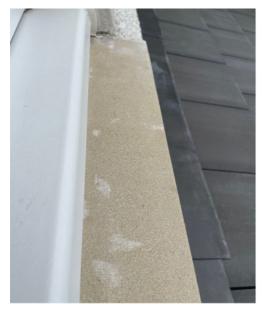

Location: General

Description: Precast window cills - render stained and overspilled.

Professionally clean to remove stains.



Location: Hall 1st Floor

Description: Window - left hand side - silicone de-bonding to cill



Location: Hall 1st Floor

Description: Wall - right hand side of bed 2 door - poor decorative finish



Location: Hall 1st Floor

Description: Cylinder cupboard vent - not level















Location: General

Description: Skirtings - review decoration throughout and make good as required.

There are areas where there are a number of paint runs evident, areas that require filling and areas that have been marked by floor fitters/hoovers.




Location: Lounge

Description: Doorstop - missing



General Location:

 $\mbox{General}$ - timber cills - dust entrapped in paint finish. Review all, sand as required and make good. Description:

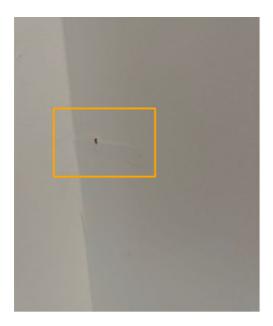

Location: Lounge

Description: Wall - left hand side of front elevation - poor decorative finish



Location: Lounge

Description: Wall - right hand side of front elevation window - plasterboard joint evident



Location: Lounge

Description: Front elevation, left hand side window - top bead damaged



Location: Lounge

Description: Lounge - window lintel - remove paint



Lounge Location:

Front elevation window - right hand side outer pane- appears to be scratched however it may be a tough stain. Clean and thereafter make good any scratches. Description:



Location: General

Description: General - radiators - tail sagging

- Lounge - Kitchen



Location: Lounge

Description: Door - poor decorative finish to low level



Location: Lounge

Description: Ceiling - plasterboard joint evident



Location: Ground floor w.c

Description: Tap - not centred on basin



Location: Ground floor w.c

Description: Basin pedestal - not straight





Ground floor w.c Location:

 \mbox{Wall} - right hand side of basin and around radiator - poor decorative finish. Paint flashing evident. Description:




Location: Ground floor w.c


Description: Wall - backing onto staircase - poor decorative finish



Location: Ground floor w.c


Description: Cistern lid - marked

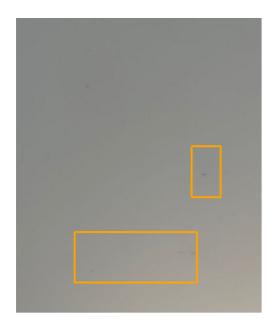

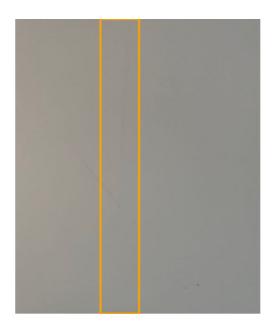

Location: Kitchen/Dining Room

Description: Ceiling - near dining room light pendant - dirty marks adjacent in a number of places.

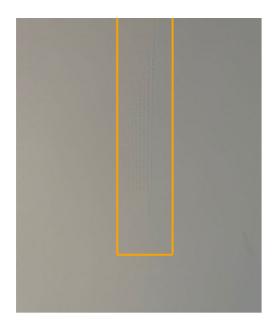





Location: Kitchen/Dining Room

Description: Ceiling - above breakfast bar - number of exposed tapes



Location: Kitchen/Dining Room

Description: Wall - left hand side of dining window - poor decorative finish



Location: Kitchen/Dining Room

Description: Double socket - left hand side of patio doors - not level



Location: Kitchen/Dining Room

Description: Pvc plate to base of patio doors - cut short on one side.



Location: Kitchen/Dining Room

Description: Left hand side patio door handle - finish chipped



Kitchen/Dining Room Location:

Left hand side patio door - clean roughcast aggregate out head of door. This is affecting the operation of the restrictor. Description:





Location: Kitchen/Dining Room

Description: Wall units - left hand side of window - paint overspilled




Location: Kitchen/Dining Room


Description: Double socket - left hand side of sink - scratched



Location: Kitchen/Dining Room

Description: Plasterboard - below wall units, left hand side of window - poor decorative finish

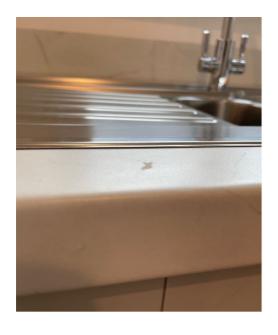

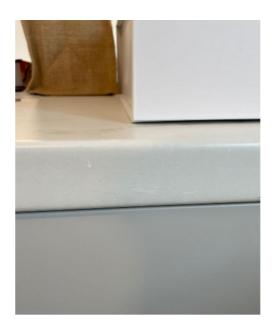

Location: Kitchen/Dining Room

Description: Worktop - front edge - paint overspilled







Location: Kitchen/Dining Room

Description: Sink and draining board - finish scratched



Location: Kitchen/Dining Room

Description: Wall unit door - left hand side of extract fan - catching infill when opening and closing




Location: Kitchen/Dining Room

Description: Wall - left hand side of extract fan - poor decorative finish



Location: Kitchen/Dining Room

Description: Door left hand side of breakfast bar - left hand side, low level - defect in finish

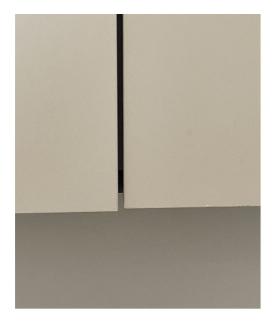


Location: Kitchen/Dining Room

Description: Breakfast bar doors - align



Location: Kitchen/Dining Room

Description: Worktop - kitchen side of breakfast bar - damaged

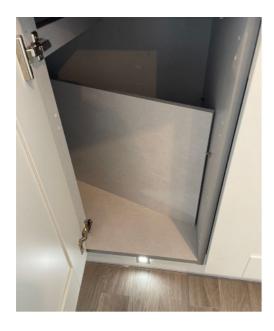

Location: Kitchen/Dining Room

Description: Base unit - left hand side of dishwasher - shelve not fitted



Location: Kitchen/Dining Room

Description: Carcass - left hand side of dishwasher - screw not fixed.



Location: Kitchen/Dining Room

Description: Dishwasher waste connection - No jubilee clip fitted






Kitchen/Dining Room Location:

Sink base unit shelve - doesn't sit on back right hand side bracket. Can't sit any further back due to position of brackets in relation to sink waste pipework. When weight is applied to the shelve this will fall. Description:



Location: Kitchen/Dining Room

Description: Door above oven - finish chipped



Location: Kitchen/Dining Room

Description: Freezer door - catching infill when opening and closing





Location: Kitchen/Dining Room

Description: Fridge door and infill panel to right hand side - paint overspilled.



Location: Kitchen/Dining Room

Description: Wall - above utility door - poor decorative finish



Location: Utility

Description: Coomb below stair - poor decorative finish



Location: Utility

Description: Window - external glass pane - number of large scratches evident



Location: Utility

Description: Draining board - scratched



Location: Utility

Description: Left hand side infill panel - chipped along base.



Location: Utility

Description: Base unit shelve - finish to underside damaged



Location: Utility

Description: Sink tap - water pressure poor




Location: Utility


Description: Larder unit - shelves missing



Location: Bed 1

Description: Door - hall side - top left hand corner - poor decorative finish

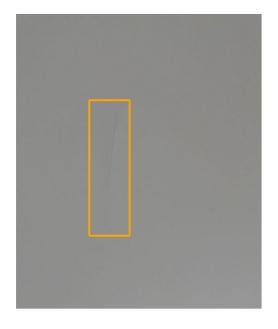





Location: Bed 1

Description: Ceiling - poor decorative finishes in a number of localised areas






Location: Bed 1

Description: Window - dirty and paint overspilled



Location: Bed 1

Description: Precast window cill - remove excess mortar



Location: Bed 1

Description: Wall - left hand side of tv point - screw head visible



Location: Bed 1

Description: Thermostat - frost risk warning present. Heating engineer to investigate and rectify .



Location: En-suite

Description: Door - bed side - top right hand side - poor decorative finish



Location: En-suite

Description: Ceiling - above shower enclosure - plasterboard joint evident




Location: En-suite

Description: Wall - right hand side of door - poor decorative finish



Location: En-suite

Description: Basin/splashback junction - poor silicone finish





Location: En-suite

Description: Shower screen - cover caps not secured

Shower screen - excess silicone



Location: En-suite

Description: Radiator - TRV - not fitted correct way round



Location: En-suite

Description: Shower waste cap - scratched



Location: En-suite

Description: Shower valves - not level





Location: Bed 4

Description: Window - protection and stickers not fully removed




Location: Bed 4

Description: Light switch - not level



Location: Bathroom

Description: Ceiling - above shower enclosure - plasterboard joints evident



Location: Bathroom

Description: External corner tape - left hand side of radiator - poor decorative finish



Location: Bathroom

Description: W.C. - finish scratched at base



Location: Bathroom

Description: Window - pvc left hand side of handle - chipped









Location: Bathroom

Description: Window - both sides of frame - silicone de-bonding



Location: Bathroom

Description: Basin - dirty

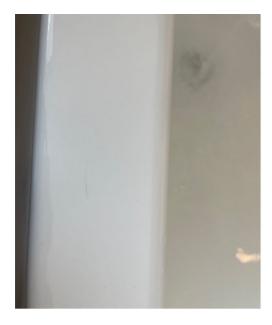

Location: Bathroom

Description: Bath - marked along front edge



Location: Bathroom

Description: Skirting - left hand side of shower tray - poorly fitted



Location: Bathroom

Description: Shower screen cover caps - not secure




Location: Bathroom

Description: Shower waste cover cap - scratched



Location: Bathroom

Description: Shower valves - not level



Bed 3 Location:

Floor - ridge evident underfoot when walking on carpet. Potentially no underlay below flooring in localised area or floor below isn't level. Housebuilder to pull back carpets, Description:

investigate and rectify



Location: Bed 2

Description: Left hand side window - bottom bead - chipped







Location: Bed 2

 $\label{lem:carpet} \textit{Carpet - appears flawed, 2no. seams evident. Carpet supplier to inspect and rectify or replace if required.}$ Description:



Location: Loft

Description: Roof - no chevron bracing fitted. Housebuilder to check their design drawings and confirm whether their should be chevron bracing fitted. If required, rectify thereafter.

BestSnag



Location: Garage

Description: Boiler flue penetration - not sealed



Location: Garage

Description: Frost stat wiring penetration - not sealed






Location: Garage


Description: Floor slab - excess mortar and plaster on floor .



Location: Front elevation

Description: Letterbox - scratched

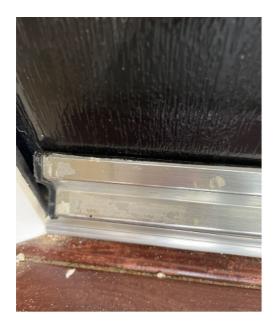

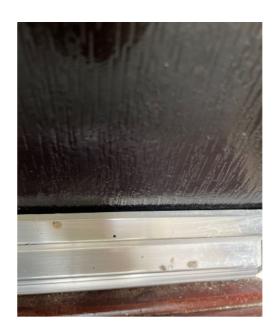

Location: Front elevation


Description: Front door weather bar - excess mortar and labels not fully removed





Location: General

Description: General - fascia's and soffits - dirty and stained in a number of areas.

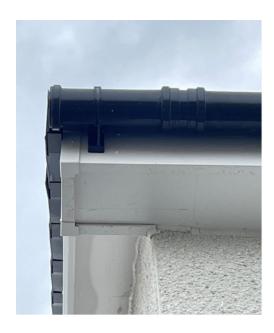

Location: Front elevation

Description: Soffit - left hand side of elevation - scratched







General Location:

Masonry pointing- pointing from 1st floor level to pine level is poor. There is excess mortar on masonry and numerous snots. The pointing is to be rectified to match the quality of the pointing at ground floor level. Description:









Location: Front elevation

Lounge window frames - dirty, marked and scratched in areas. Clean and thereafter make good any damage. \\ Description:



Location: Front elevation

Description: Masonry - excess mortar below lounge precast cill



Location: Front elevation

Description: Masonry pointing - right hand side of elevation - localised holes



Location: Front elevation

Description: Render - below bed 2 precast cill - poorly finished



Location: Front elevation

Description: Excess protection to be removed below belcast bead






Location: Front elevation

Description: Weep vents at base of render missing to lead cavity tray



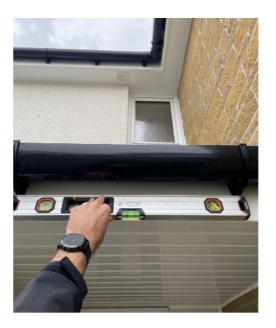



Location: Front elevation

Description: Low level roof - gutter - falls away from outlet instead of towards outlet.



Location: Front elevation

Description: Masonry - left hand side of garage door - dpc exposed



Location: Side elevation facing no.3

Description: Leadwork - stained



Location: Side elevation facing no.3

Description: Render - belcast bead runs continuous through movement joint



Location: Side elevation facing no.3

Description: Boiler flue - cover cap missing



Location: Side elevation facing no.3

Description: Electric box - damaged





Location: Side elevation facing no.3

Description: Render - obvious patch repairs to roughcast



Side elevation facing footpath Location:

Description: Render - stained at pine - remnants of a bird nest.



Side elevation facing footpath Location:

Weep vent - right hand side of utility window cill - blocked with render Description:







Location: General

General - external windows and frames - pvc is marked, dirty and scratched in areas. Clean all and thereafter make good any damage. Description:




Side elevation facing footpath Location:


Description: Lounge precast window cill - left hand side chipped



Location: Rear elevation

Description: Roof tiles- bottom course - local tile damaged left hand side of waste stack

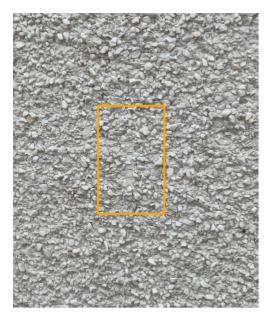

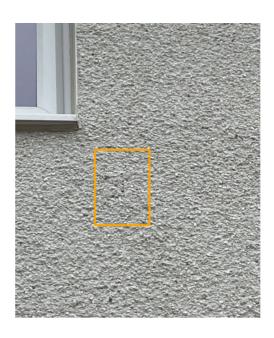





Location: Rear elevation

Description: Weep vents - number are blocked with render

-left hand side of dining window cill- right hand side of bed 3 window cill- right hand side of bathroom window cill- both below kitchen window





Location: Rear elevation

Description: Patio door hinges - mortar overspilled

Patio door hinge - top right hand side - finish chipped



Location: Rear elevation

Description: Masonry band course - dirt stained




Location: Rear elevation

Description: Downpipe - not plumb



Location: Rear grounds

Description: Rodding point - not level with ground

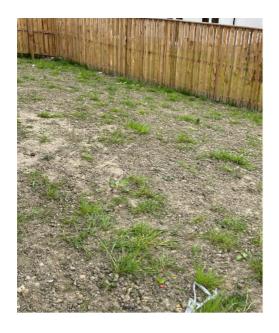



Location: Rear grounds

Description: Soil - weeds evident. Weed and rotivate garden.



Location: Rear grounds

Description: Soil - remove rod



Location: Decking

Description: Decking handrail - localised section has split



Location: Side grounds

Description: Patch - excessive gaps between paving slabs





Location: Front grounds

Description: Landscaping - perimeter hedge still to be planted
